


Footage	% Recovery		% Copper		
	Core	Sludge	Core	Sludge	Accepted
64 - 68	75			0.19	
68 - 71	95	108	2.10	0.71	1.18
71 - 72	95				0.56
72 - 75	95		0.15	0.56	0.42
75 - 77½	67		3.50		1.59
77½ - 79	67	44	0.30	0.99	0.83
79 - 85	28	61	2.00	0.85	0.96
85 - 86½	61			0.50	0.50
86½ - 88	61	141	1.50	1.90	1.81
88 - 90	79	33	1.65	1.65	1.65
90 - 92	79		1.00		
92 - 96				0.90	
96 - 97	44		0.65		
119 - 124	13			0.20	
182½ - 191	84			0.50	
213 - 214	75				
214 - 215½			0.90		1.93
215½ - 217½	75		9.00	2.30	4.08
217½ - 219			2.00		2.22

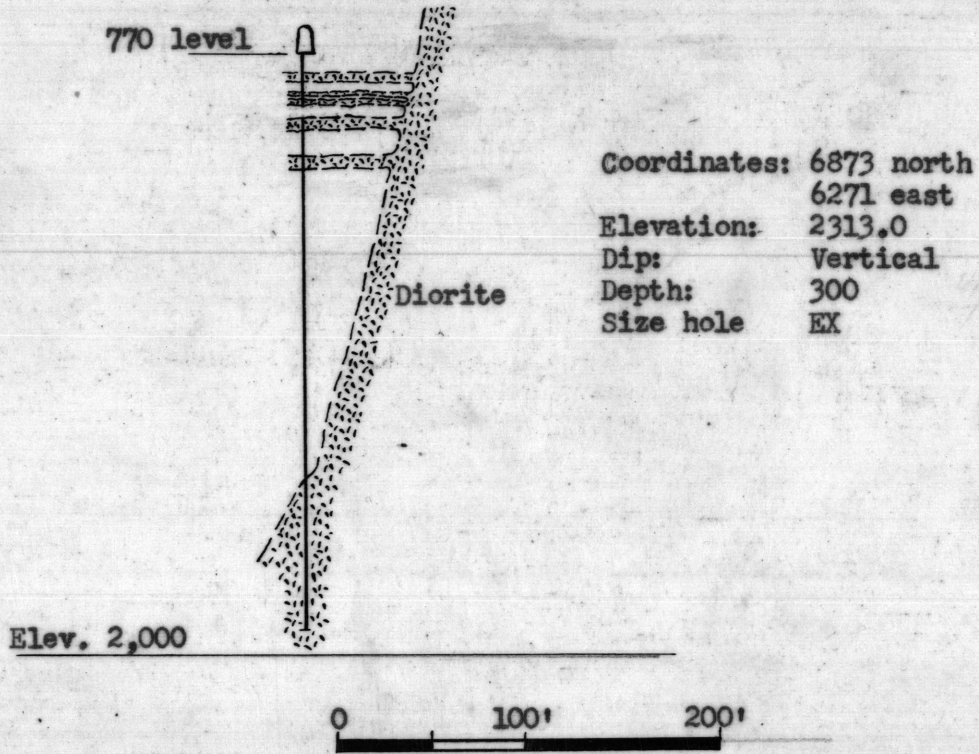

CHRISTMAS PROJECT 1419

Fig. 38 . MUDD DIAMOND DRILL HOLE 56-A
