



Footage	% Recovery		% Copper		
	Core	Sludge	Core	Sludge	Accepted
0 - 18	28		0.26		
13 - 18	28			3.00	3.00
18 - 25	29	214	5.40	2.05	2.40
25 - 27	29		0.21		1.86
27 - 34	29	121	1.03	1.48	1.43
34 - 41	12	176	0.08	4.07	3.90
71 - 74	100	222	2.06	1.73	2.06
74 - 83	33	213	2.52	0.90	2.52
83 - 88	100			0.36	
88 - 94	100			0.25	
94 - 98	25			0.51	
98 - 104	50			0.80	
104 - 112	67	130	0.93	0.61	
112 - 117	10	84	0.38	0.80	
117 - 118	50			0.30	
118 - 125	50	150	0.46	0.85	
125 - 130	43		0.21		
134 - 136				0.82	0.93
136 - 136½	21		2.31	4.85	4.66
136½ - 138				0.41	0.55
138 - 145	85		1.70	0.71	1.01

Coordinates: 6862 north
6518 east
Elevation: 2313.0
Bearing: North 12 east
Dip: Minus 80
Depth: 344
Size hole: EX

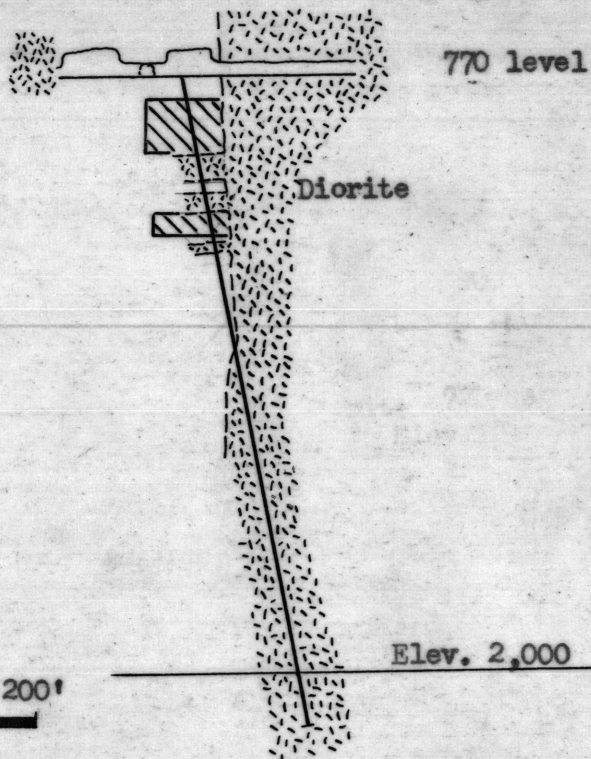

Ore blocks



CHRISTMAS PROJECT 1419

Fig. 36 . MUDD DIAMOND DRILL HOLE 52-B
