


Footage	% Recovery		% Copper		
	Core	Sludge	Core	Sludge	Accepted
100 - 110	30			1.03	
110 - 117				3.13	3.13
117 - 124	3	178	3.30	1.91	1.93
124 - 125				2.95	2.95
125 - 126				4.52	3.23
126 - 129	100		0.90		2.22
129 - 129.3				2.94	2.51
129.3-132	63		1.00	2.95	2.51
132 - 133					
134 - 141	44		0.40		
184 - 189	0			2.52	2.52
189 - 194	3		0.10	1.85	1.83
194 - 199	30		5.30	2.15	2.49
199 - 204	10		2.90	2.27	2.29
204 - 209	13		1.00	2.78	2.70
227 - 235				0.41	
235 - 237				0.62	
237 - 242				0.20	
242 - 248				0.41	
284 - 288				1.44	
288 - 292				1.03	
292 - 293				0.71	
293 - 295				1.03	
295 - 299				0.92	

770 level

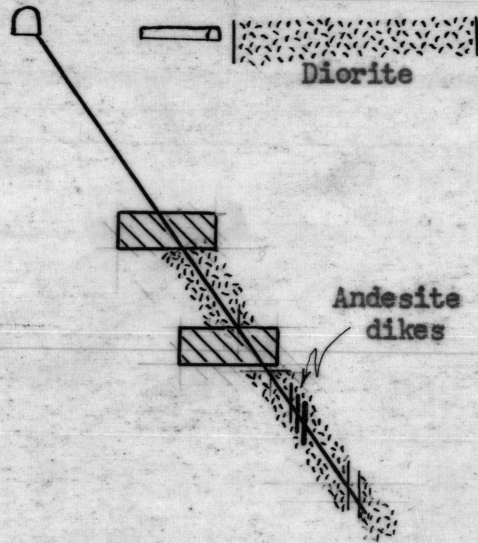

Coordinates: 7207 north  
5973 east  
Elevation: 2313.0  
Bearing: South 45 east  
Dip: Minus 55  
Depth: 299  
Size hole: EX

Elev. 2,000

0 100' 200'

CHRISTMAS PROJECT 1419

Fig. 39. MUDD DIAMOND DRILL HOLE 57-A
