FINAL REPORT

No.	Level	Description	Width ft.	Gold oz. per Ton	Silver	Value $
40	Shaft	Quartz Only	0.8	0.60	–	19.32
41	"	"	0.5	0.22	0.06	7.12
42	310	"	0.8	0.30	–	9.66
43	"	"	0.6	0.08	–	2.57
44	"	"	0.5	0.03	0.01	0.98
45	"	"	0.6	1.00	0.10	32.26
46	Shaft	"	0.6	0.12	0.10	3.92
47	"	"	0.9	0.50	0.30	16.28
48	"	"	0.7	0.16	0.08	5.20
49	230	"	0.7	1.82	0.28	58.77
50	"	"	1.1	0.92	0.28	29.89
51	"	"	0.9	0.09	–	2.89
52	"	"	0.8	0.05	–	1.62
53	"	"	0.6	0.03	–	0.96
54	"	"	0.7	0.06	–	1.93
55	"	"	0.6	0.50	0.30	16.28
56	Shaft	"	0.8	0.50	0.10	16.16
57	"	"	0.4	0.52	0.08	16.79

Av. without (item X) · 16.31

Av. with (Item X) → 20.95

FINAL REPORT

No.	Level	Description	Width ft.	Gold oz. per Ton	Silver	Value $
21	230	Quartz only	0.8	0.04	0.02	1.31
22	"	" Little Schist	1.0	0.40	–	12.87
23	"	Nearly All Schist	1.1	0.03	–	0.96
24	"	Quartz only	1.3	0.51	–	16.42
25	"	"	1.1	0.12	–	3.86
26	Shaft	"	0.8	0.26	–	8.37
27	"	"	0.8	0.52	–	16.74
28	"	"	1.0	0.62	–	19.96
29	"	"	0.9	0.03	–	0.96
30	280	" and Schist	1.0	0.20	–	6.42
31	"	" only	1.8	0.10	–	3.22
32	"	" and Little Schist	0.5	2.50	–	80.50
33	"	" Schist	1.4	0.18	0.10	5.85
34	"	" only	1.1	0.60	0.40	19.57
35	"	" High Grade Pocket X	8.56	0.54		275.97
36	310	"	1.5	0.36	0.34	11.80
37	"	"	1.3	0.04	–	1.28
38	"	"	0.6	0.20	0.20	6.56
39	"	"	0.4	0.02	0.18	0.75

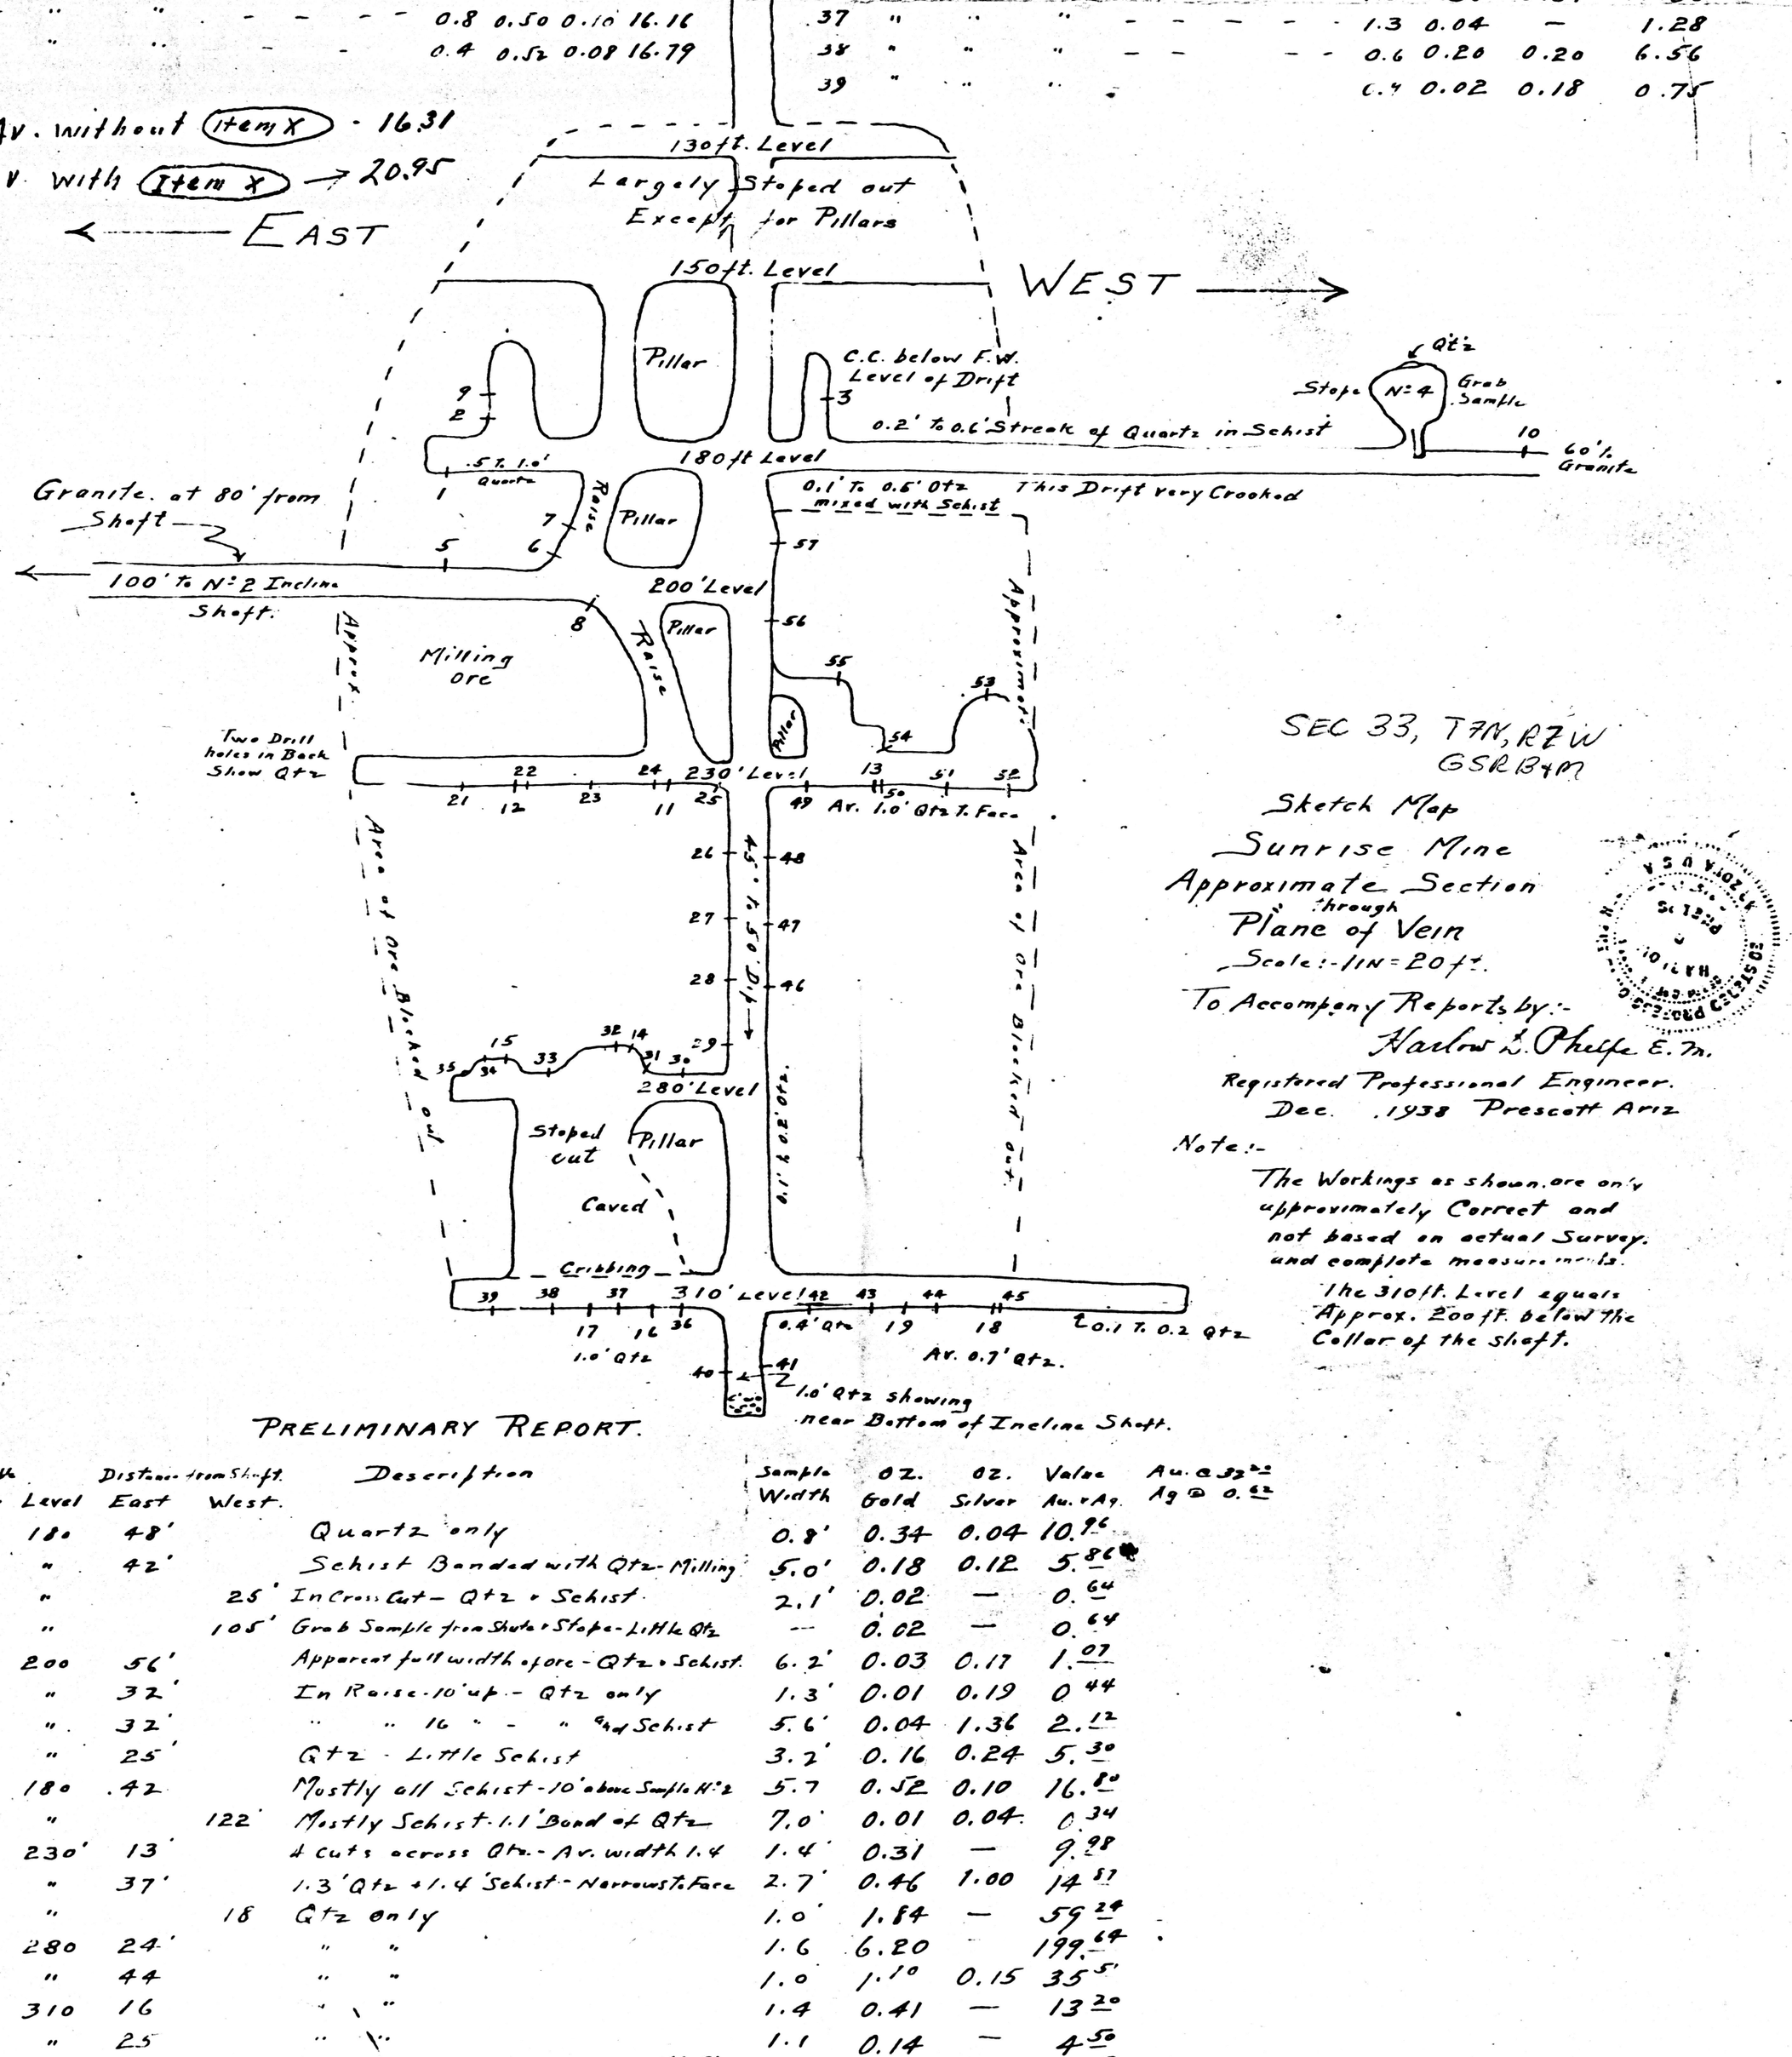

SEC 33, T7N, R2W
GSR&M

Sketch Map
Sunrise Mine
Approximate Section through Plane of Vein
Scale:- 1IN = 20ft.
To Accompany Reports by:-
Harlow D. Phelps E.M.
Registered Professional Engineer.
Dec. 1938 Prescott Ariz

Note:-
The Workings as shown are only approximately Correct and not based on actual Survey. and complete measurements.
The 310ft. Level equals Approx. 200ft. below the Collar of the Shaft.

PRELIMINARY REPORT.

Sample No.	Level	Distance from Shaft East	Distance from Shaft West	Description	Sample Width	oz. Gold	oz. Silver	Value Au. + Ag.
1	180	48'		Quartz only	0.8'	0.34	0.04	10.96
2	"	42'		Schist Banded with Qtz - Milling	5.0'	0.18	0.12	5.86
3	"		25'	In Cross Cut - Qtz + Schist	2.1'	0.02	–	0.64
4	"		105'	Grab Sample from Shute + Stope - Little Qtz	–	0.02	–	0.64
5	200	56'		Apparent full width of ore - Qtz + Schist	6.2'	0.03	0.17	1.07
6	"	32'		In Raise - 10' up - Qtz only	1.3'	0.01	0.19	0.44
7	"	32'		" " 16' " - " and Schist	5.6'	0.04	1.36	2.12
8	"	25'		Qtz - Little Schist	3.2'	0.16	0.24	5.30
9	180	42		Mostly all Schist - 10' above Sample No 2	5.7	0.52	0.10	16.80
10	"		122'	Mostly Schist - 1.1' Band of Qtz	7.0'	0.01	0.04	0.34
11	230'	13'		4 Cuts across Qtz. - Av. width 1.4	1.4'	0.31	–	9.98
12	"	37'		1.3' Qtz + 1.4' Schist - Narrows to Face	2.7'	0.46	1.00	14.51
13	"		18	Qtz only	1.0'	1.84	–	59.24
14	280	24'		" "	1.6	6.20		199.64
15	"	44		" "	1.0	1.10	0.15	35.50
16	310	16		" "	1.4	0.41	–	13.20
17	"	25		" "	1.1	0.14	–	4.50
18	"		39	1.0' Qtz + 2.0' Schist Little Qtz in Schist	3.0	0.14	0.06	4.50
19	"		25	Quartz Only - Cuts - Av. width 0.7'	0.7	0.62	0.28	20.30
20				Grab Sample from Sorted ore from Dump		1.23	–	39.60

Au. @ $32.00
Ag @ 0.62
